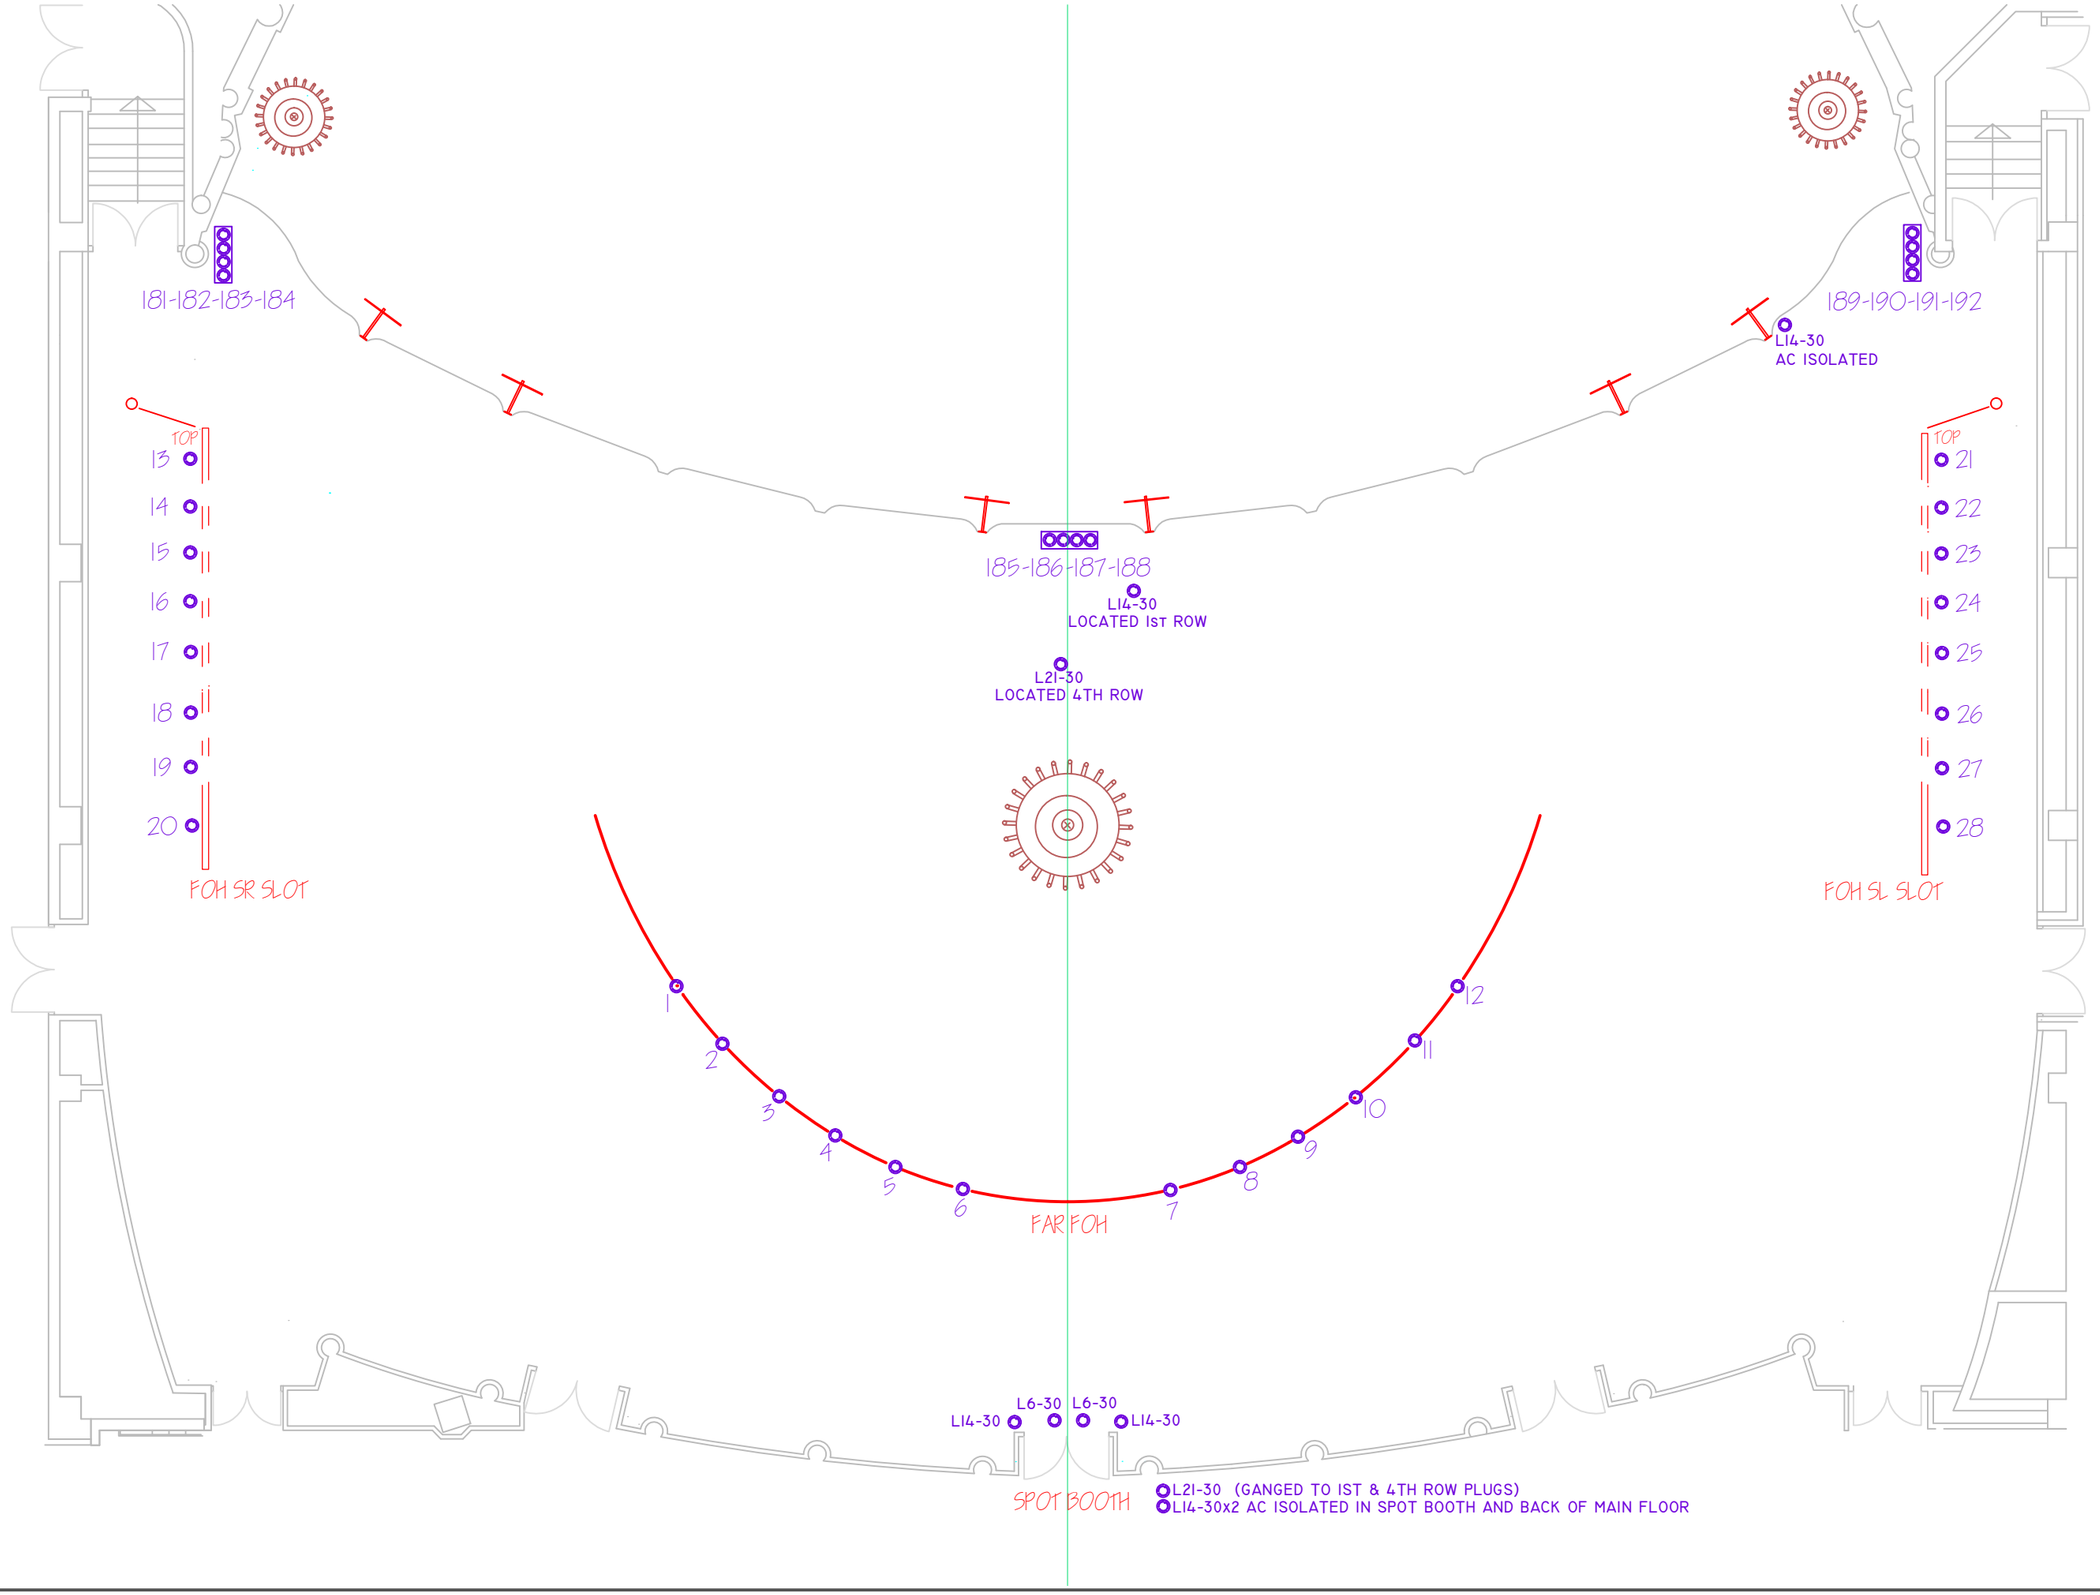

HOUSE LIGHT DIMMERS

193 - Under Balcony Mini Chand.
194 - Main Huge Chandelier
195 - Under Balcony Wall Sconces
196 - high loft chandeliers
197 - Balcony Wall Sconces
198+199+200 Dome Fresco
201 - Organ Loft High Chandeliers
202 - Not Used
203 - Not Used
204 - Not Used
205 - Balcony Ceiling Pars/Pots
206 - LED Ceiling Architecture
207 - Under Balcony Pots
208 - Under Balcony cove/Dome
233 - under balcony wall pots

ORPHEUM

Circuit Plot 2016

Orpheum Theatre - FOH

192 Dimmers + LED Units

48 Houselight Dimmers - On Linked System

LX Plot By: B. Keith	1 of 2
Technical Director: M. Muir	
Head Carp: P. McManus	
Date: Dec 1, 2016	
Scale:	Revision: 5

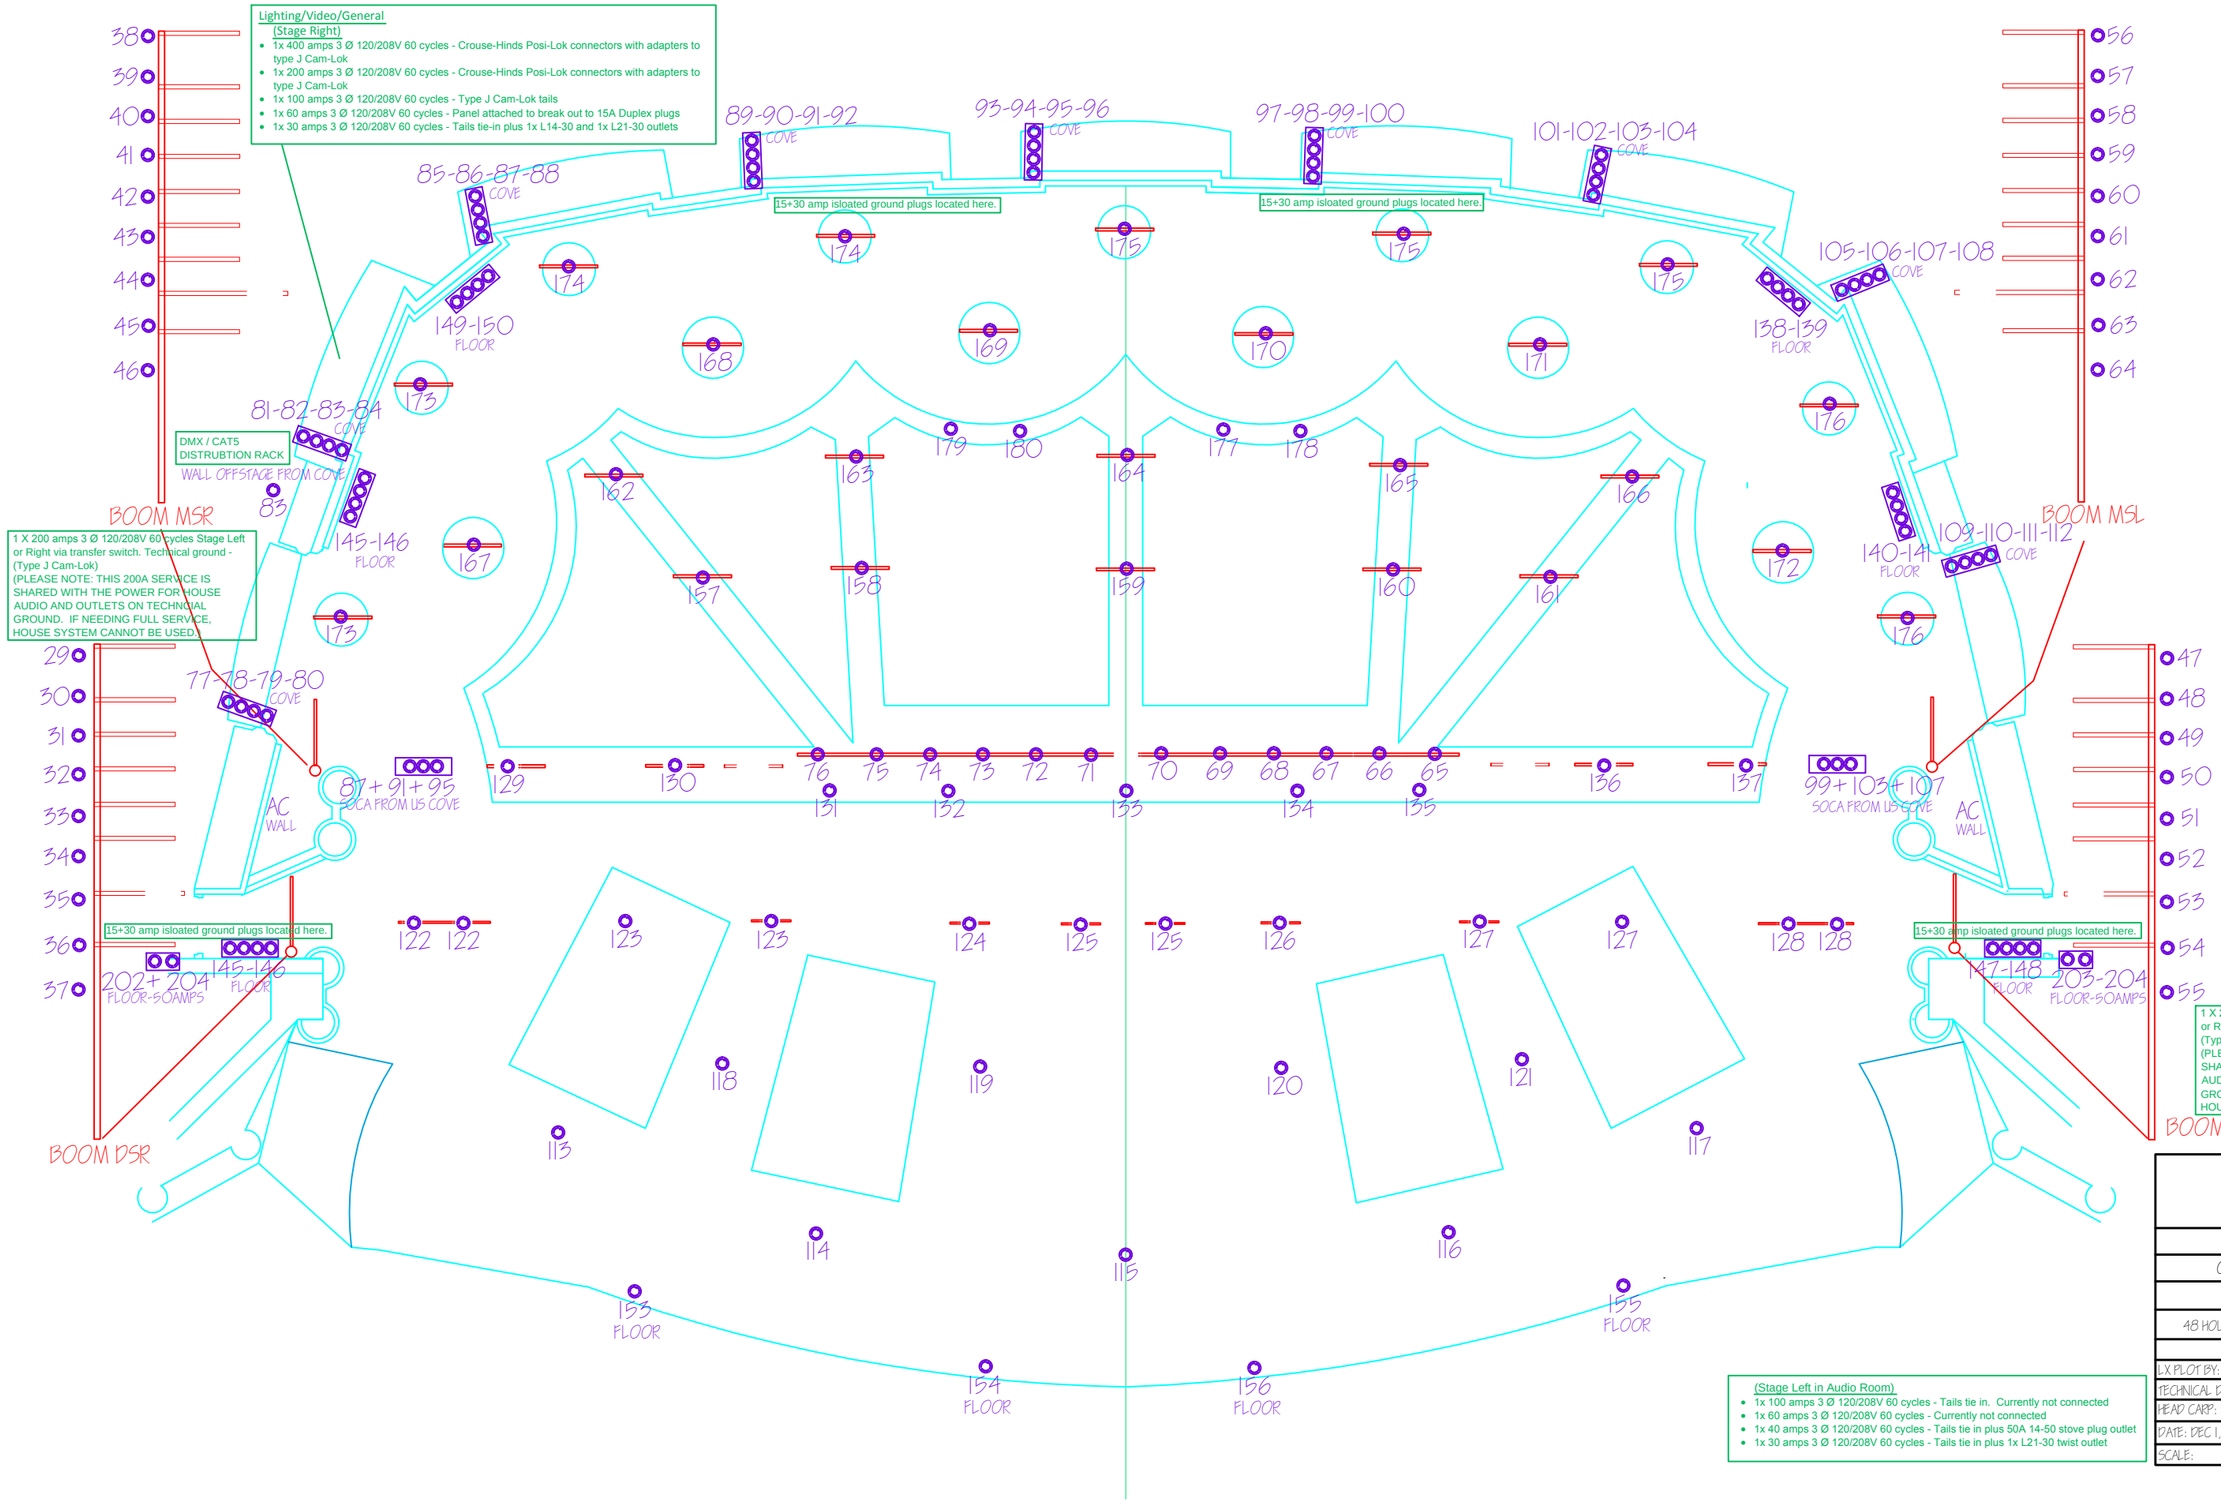
Lighting/Video/General
(Stage Right)
1x 400 amps 3 Ø 120/208V 60 cycles - Crouse-Hinds Posi-Lok connectors with adapters to type J Cam-Lok
1x 200 amps 3 Ø 120/208V 60 cycles - Crouse-Hinds Posi-Lok connectors with adapters to type J Cam-Lok
1x 100 amps 3 Ø 120/208V 60 cycles - Type J Cam-Lok tails
1x 60 amps 3 Ø 120/208V 60 cycles - Panel attached to break out to 15A Duplex plugs
1x 30 amps 3 Ø 120/208V 60 cycles - Tails tie-in plus 1x L14-30 and 1x L21-30 outlets
15+30 amp isloated ground plugs located here.
15+30 amp isloated ground plugs located here.
DMX / CAT5 DISTRUBTION RACK
WALL OFFSTAGE FROM COVE
1 X 200 amps 3 Ø 120/208V 60 cycles Stage Left or Right via transfer switch. Technical ground - (Type J Cam-Lok)
(PLEASE NOTE: THIS 200A SERVICE IS SHARED WITH THE POWER FOR HOUSE AUDIO AND OUTLETS ON TECHNCIAL GROUND. IF NEEDING FULL SERVICE, HOUSE SYSTEM CANNOT BE USED.)
BOOM MSR
BOOM MSL
BOOM DSR
BOOM DSL
89-90-91-92 COVE
93-94-95-96 COVE
97-98-99-100 COVE
101-102-103-104 COVE
85-86-87-88 COVE
105-106-107-108 COVE
149-150 FLOOR
138-139 FLOOR
81-82-83-84 COVE
145-146 FLOOR
140-141 FLOOR
109-110-111-112 COVE
77-78-79-80 COVE
87+91+95 SOCA FROM US COVE
99+103+107 SOCA FROM US COVE
AC WALL
AC WALL
15+30 amp isloated ground plugs located here.
15+30 amp isloated ground plugs located here.
202+204 FLOOR-50AMPS
145-146 FLOOR
147-148 FLOOR
203-204 FLOOR-50AMPS
153 FLOOR
154 FLOOR
155 FLOOR
156 FLOOR
1 X 200 amps 3 Ø 120/208V 60 cycles Stage Left or Right via transfer switch. Technical ground - (Type J Cam-Lok)
(PLEASE NOTE: THIS 200A SERVICE IS SHARED WITH THE POWER FOR HOUSE AUDIO AND OUTLETS ON TECHNCIAL GROUND. IF NEEDING FULL SERVICE, HOUSE SYSTEM CANNOT BE USED.)
(Stage Left in Audio Room)
1x 100 amps 3 Ø 120/208V 60 cycles - Tails tie in. Currently not connected
1x 60 amps 3 Ø 120/208V 60 cycles - Currently not connected
1x 40 amps 3 Ø 120/208V 60 cycles - Tails tie in plus 50A 14-50 stove plug outlet
1x 30 amps 3 Ø 120/208V 60 cycles - Tails tie in plus 1x L21-30 twist outlet
ORPHEUM
CIRCUIT PLOT 2016
ORPHEUM THEATRE - STAGE
192 DIMMERS + LED UNITS
48 HOUSELIGHT DIMMERS - ON LINKED SYSTEM
LX PLOT BY: B. KEITH
TECHNICAL DIRECTOR: M. MUIR
HEAD CARP.: P. MCMANUS
DATE: DEC 1, 2016
SCALE:
2 OF 2
REVISION: 5
